


ID	Task Name	Duration	% Complete	Early Start	Early Finish	Total Float	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
150	Install Guardrail West Approach	1 day	100%	Mon 6/6/11	Tue 6/7/11	0 days																										
154	Remove Existing Bridge Between Utility Poles	5 days	10%	Tue 6/7/11	Thu 6/16/11	51.5 days																										
153	Switch Utilities to New Conduit and Poles	35 days	0%	Fri 6/10/11	Thu 7/28/11	0 days																										
164	Remove Remainder of Existing Bridge	10 days	0%	Fri 7/29/11	Thu 8/11/11	0 days																										
155	Rebuild North Boat Ramp Parking Area and Surface Pave	3 days	0%	Fri 8/12/11	Tue 8/16/11	0 days																										
163	Finish Guardrail	2 days	0%	Wed 8/17/11	Thu 8/18/11	0 days																										
156	Clean Up and Punch List	5 days	0%	Fri 8/19/11	Thu 8/25/11	0 days																										
157	Project Completion	1 day	0%	Fri 8/26/11	Fri 8/26/11	0 days																										

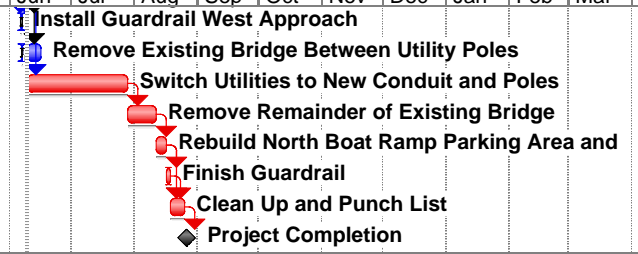

KNICKERBOCKER BRIDGE over
BACK RIVER
Updated Thu 6/9/11

Task		Summary		Rolled Up Progress		Group By Summary	
Critical Task		Rolled Up Task		Split		Deadline	
Progress		Rolled Up Critical Task		External Tasks			
Milestone		Rolled Up Milestone		Project Summary			
