Project Manager: MPavlic
Project Start: 09Mar2012
Project Finish: 15May201
Time Now: 05/10/2012
Run: 10May2012

Allegheny County
Allegheny Co MT06
Allegheny Co MT06

Planned
Critical
Late Dates
Milestone
Progress
Summary
Float
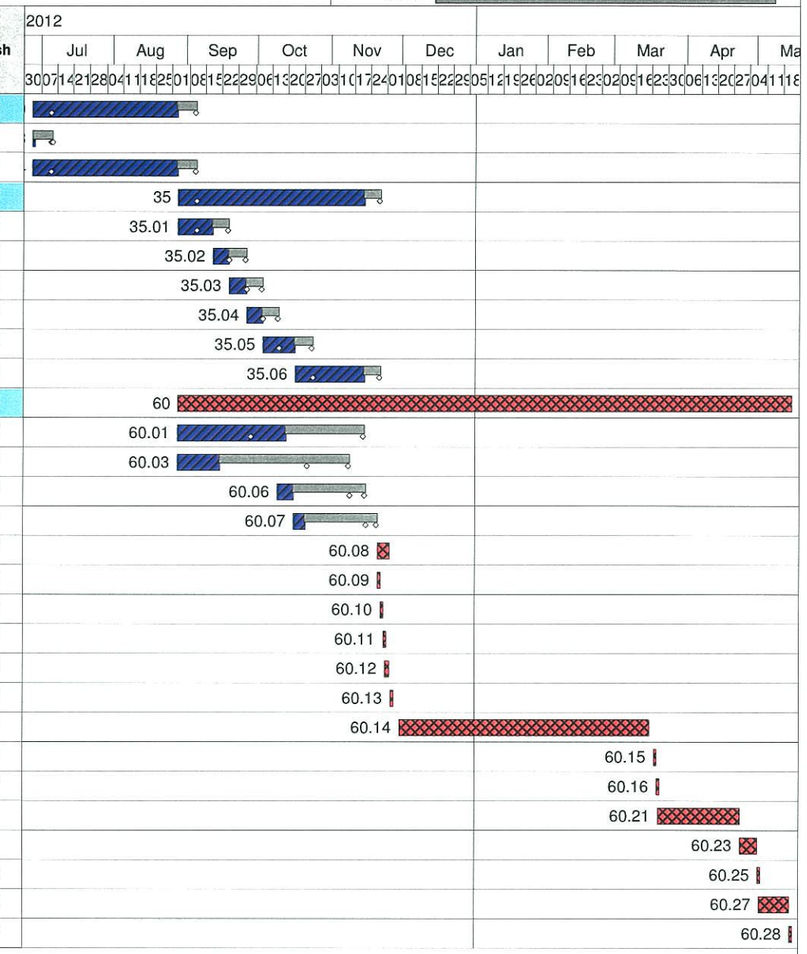
Activity ID	Activity Desc.	Duration	Total Float	Early Start	Early Finish	gress_Perc	Actual Start	Actual Finish	Late Start	Late Finish
10	Administration	62d	6d	27Jun2012	27Aug2012	0			05Jul2012	04Sep2012
10.3	LET	0	6d	27Jun2012	27Jun2012	0			05Jul2012	05Jul2012
10.4	Notice to Proceed	44d	6d	27Jun2012	27Aug2012	0			05Jul2012	04Sep2012
35	Fabrication	56d	5d	28Aug2012	14Nov2012	0			05Sep2012	21Nov2012
35.01	Prepare/Submit Beams, Grid Deck & Brg Pads Shop Drawings	10d	5d	28Aug2012	11Sep2012	0			05Sep2012	18Sep2012
35.02	Review/Comment Beam, Grid Deck & Brg Pads Shop Drawings	5d	5d	12Sep2012	18Sep2012	0			19Sep2012	25Sep2012
35.03	Revise/Resubmit Beam, Grid Deck & Brg Pads Shop Drawings	5d	5d	19Sep2012	25Sep2012	0			26Sep2012	02Oct2012
35.04	Review/Approve Beam, Grid Deck & Brg Pads Shop Drawings	5d	5d	26Sep2012	02Oct2012	0			03Oct2012	09Oct2012
35.05	Fabricate Beams	10d	5d	03Oct2012	16Oct2012	0			10Oct2012	23Oct2012
35.06	Fabricate Precast Cap & Deck Sections	21d	5d	17Oct2012	14Nov2012	0			24Oct2012	21Nov2012
60	Construction	222d	0	28Aug2012	15May2013	0			28Sep2012	15May2013
60.01	Material Acquisition	34d	23d	28Aug2012	12Oct2012	0			28Sep2012	14Nov2012
60.03	14 day Advance Warning	14d	39d	28Aug2012	14Sep2012	0			22Oct2012	08Nov2012
60.06	Mobilization	5d	23d	09Oct2012	15Oct2012	0			09Nov2012	15Nov2012
60.07	Construct Erosion and Sedimentation Control Plan	5d	31d	16Oct2012	20Oct2012	0			16Nov2012	20Nov2012
60.08	Implement Phase 1 MPT	5d	0	21Nov2012	25Nov2012	0			21Nov2012	25Nov2012
60.09	Superstructure/Partial Abutment Demolition	1d	0	21Nov2012	21Nov2012	0			21Nov2012	21Nov2012
60.10	Install Abutment Caps	1d	0	22Nov2012	22Nov2012	0			22Nov2012	22Nov2012
60.11	Place Class R7 Rock Rip Rap	1d	0	23Nov2012	23Nov2012	0			23Nov2012	23Nov2012
60.12	Set Superstructure and Closure Pour	2d	0	24Nov2012	25Nov2012	0			24Nov2012	25Nov2012
60.13	Completion Milestone	0	0	26Nov2012	26Nov2012	0			26Nov2012	26Nov2012
60.14	Winter Shutdown	0	0	30Nov2012	15Mar2013	0			30Nov2012	15Mar2013
60.15	Implement Phase 2 MPT/Switch Traffic	1d	0	18Mar2013	18Mar2013	0			18Mar2013	18Mar2013
60.16	Construct Erosion & Sedimentation Control Plan for Approach Roadway	1d	0	19Mar2013	19Mar2013	0			19Mar2013	19Mar2013
60.21	Construct Approach Roadway	25d	0	20Mar2013	23Apr2013	0			20Mar2013	23Apr2013
60.23	Pavement Markings and Signing	5d	0	24Apr2013	30Apr2013	0			24Apr2013	30Apr2013
60.25	Remove MPT	1d	0	01May2013	01May2013	0			01May2013	01May2013
60.27	Final Project Cleanup/Demobilization	9d	0	02May2013	14May2013	0			02May2013	15May2013
60.28	Final Project Completion (Milestone Date)	0	0	15May2013	15May2013	0			15May2013	15May2013
